

STATEMENT OF QUALIFICATIONS

PART I – CONTRACT SPECIFIC QUALIFICATIONS

A. CONTRACT INFORMATION

1. PROJECT TITLE AND LOCATION (City and State)
 Claims Analysis / Dispute Resolution Consultant List

| | |
|---------------------------------------|----------------------------------|
| 2. ANNOUNCEMENT DATE March 4, 2011 | 3. PROJECT NUMBER DAS-11 D888 |
|---------------------------------------|----------------------------------|

B. FIRM POINT OF CONTACT

| | |
|---|---|
| 4. PROJECT REPRESENTATIVE NAME AND TITLE Dennis Jasinski, Project Director | 5. PRESIDENT / CEO William R Zollinger III, PE |
|---|---|

6. NAME OF FIRM
 R.V. Buric Construction Management Consultants, Inc.

| | | |
|---------------------------------------|---------------------------------|--|
| 7. TELEPHONE NUMBER (440) 247-3700 | 8. FAX NUMBER (440) 247-5022 | 9. E-MAIL ADDRESS djasinski@buric.com |
|---------------------------------------|---------------------------------|--|

| | | |
|----------------------|-------------------------------|----------------------------------|
| 10. COUNTY Geauga | 11. FTID NUMBER [REDACTED] | 12. WEB ADDRESS www.buric.com |
|----------------------|-------------------------------|----------------------------------|

C. PROPOSED TEAM

(Complete this section for the lead firm or joint venture partners, and all key consultants.)


| (Check) | | | 13. FIRM NAME | 14. ADDRESS | 15. ROLE IN THIS CONTRACT |
|-----------|-------------------------------------|--------------------------|--|---|---|
| Lead Firm | JV Partner | Consultant | | | |
| a. | <input checked="" type="checkbox"/> | <input type="checkbox"/> | R.V. Buric Construction Management Consultants, Inc. <input type="checkbox"/> Check if EDGE certified | 300 Park Place Chagrin Falls, OH 44022 <input type="checkbox"/> Check if branch office ___ Miles from project site | Claims Analysis/Dispute Resolution Services |
| b. | <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> Check if EDGE certified | <input type="checkbox"/> Check if branch office | |
| c. | <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> Check if EDGE certified | <input type="checkbox"/> Check if branch office | |
| d. | <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> Check if EDGE certified | <input type="checkbox"/> Check if branch office | |
| e. | <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> Check if EDGE certified | <input type="checkbox"/> Check if branch office | |
| f. | <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> Check if EDGE certified | <input type="checkbox"/> Check if branch office | |

D. ORGANIZATIONAL CHART OF PROPOSED TEAM

(Attached)

INSERT ORGANIZATIONAL CHART BELOW OR ATTACH.

BURIC'S ORGANIZATIONAL CHART OF PROPOSED TEAM

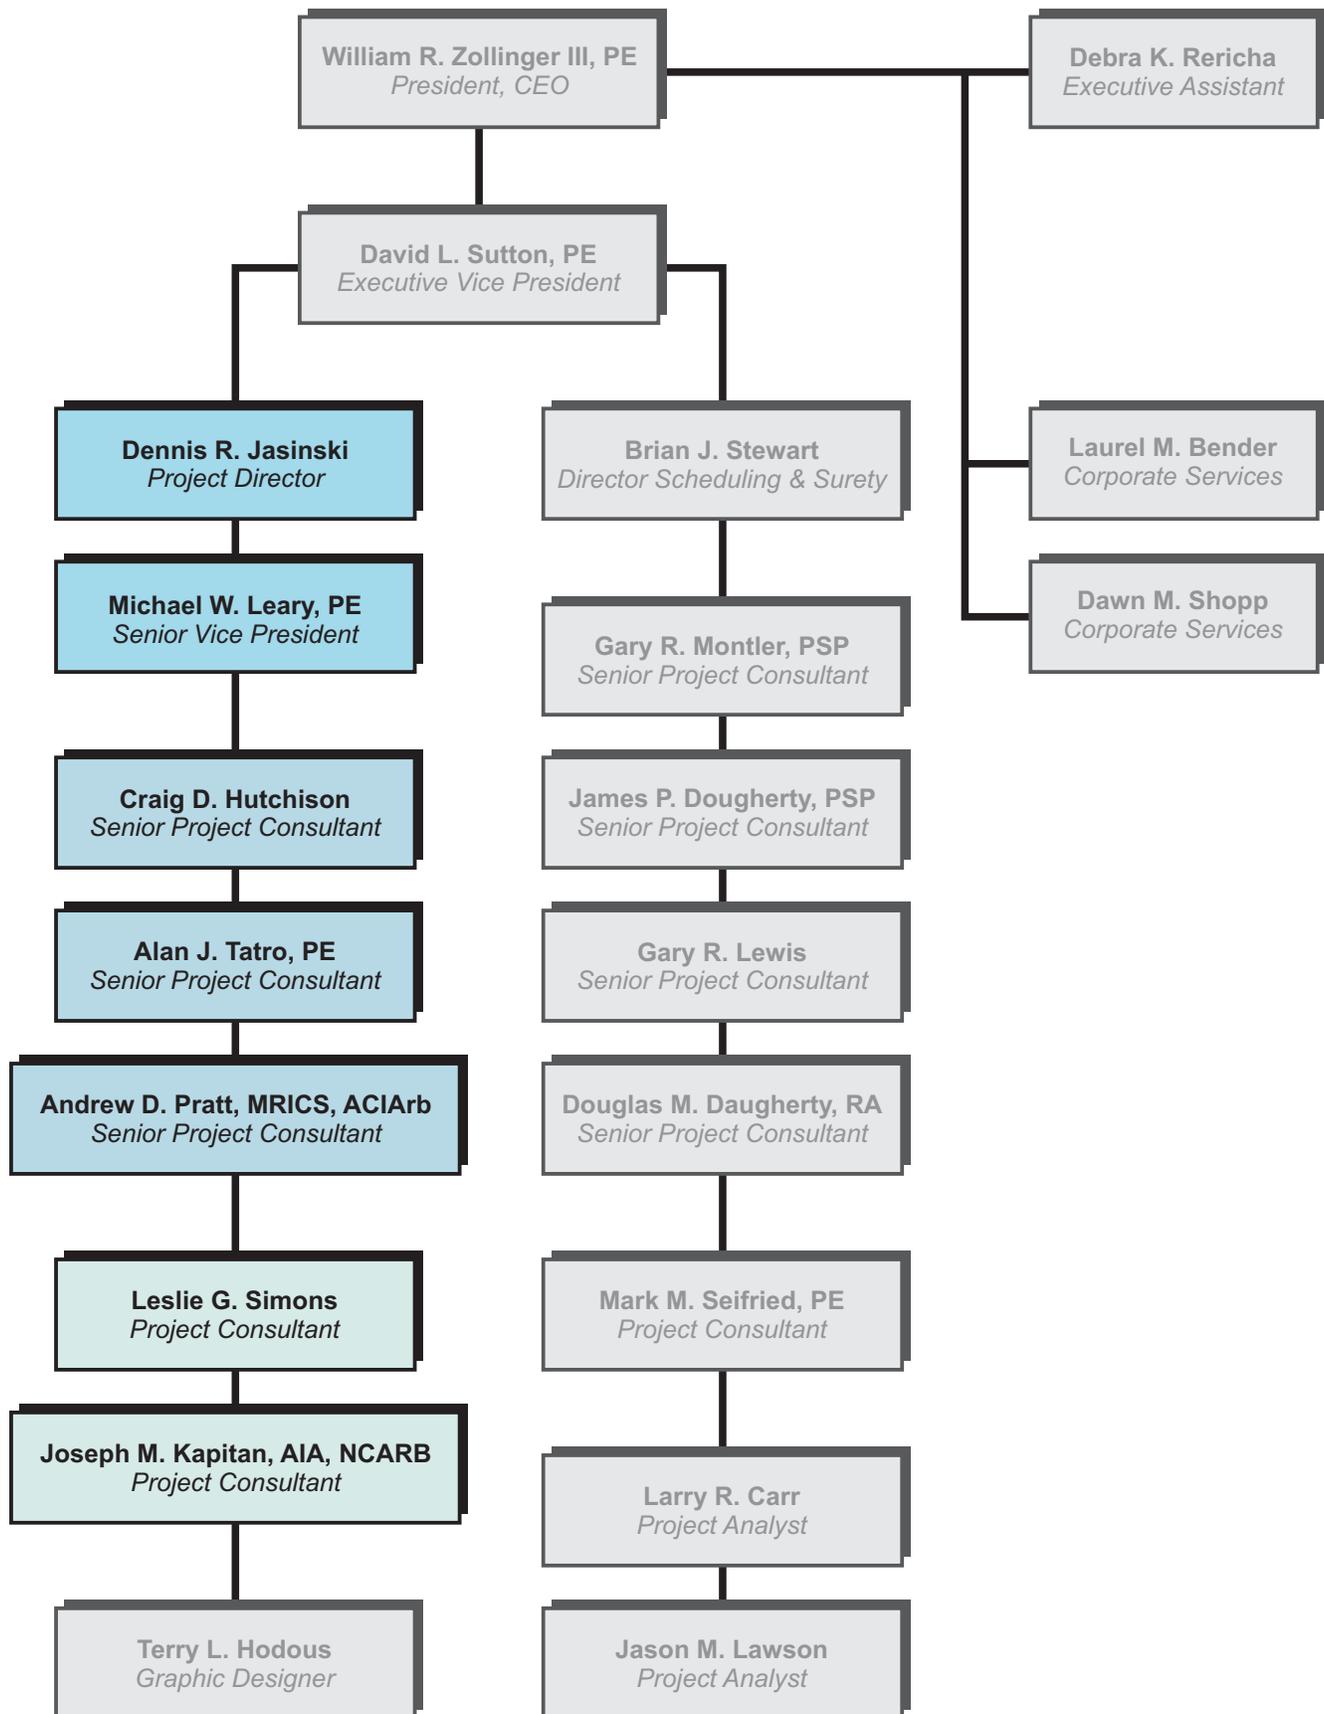

E. RESUMES OF KEY PERSONNEL PROPOSED FOR THIS CONTRACT

(Complete one Section E for each key person.)

| | | | |
|----------------------------------|--|----------------------|----------------------------|
| 16. NAME Michael W. Leary, PE | 17. ROLE IN THIS CONTRACT Project Lead / Expert Witness | 18. YEARS EXPERIENCE | |
| | | a. TOTAL 31 | b. WITH CURRENT FIRM 27 |

19. FIRM NAME AND LOCATION (City and State)
RV Buric Construction Management Consultants, Inc. Chagrin Falls, OH

| | |
|---|---|
| 20. EDUCATION (DEGREE AND SPECIALIZATION) BS Civil Engineering | 21. CURRENT PROFESSIONAL REGISTRATION (STATE AND DISCIPLINE) Ohio Registered Professional Civil Engineer |
|---|---|

22. OTHER PROFESSIONAL QUALIFICATIONS (Publications, Organizations, Training, Awards, etc.)
AAA – Panel of Arbitrators, AACEi, ASCE / Publications for AACEi and Construction Claims Superconference

23. RELEVANT PROJECTS (Up to a maximum of 5 samples)

| (1) TITLE AND LOCATION (City and State) | (2) YEAR COMPLETED | | (3) EXAMPLE PROJECT KEY NUMBER (If included in Section F) |
|---|-------------------------------|--------------------------------------|---|
| | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| a. (1) TITLE AND LOCATION (City and State) Case Western Reserve University North Residential Village Cleveland, OH | PROFESSIONAL SERVICES 2007 | CONSTRUCTION (If applicable) 2005 | 3 |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Lead claims analyst for schedule and damages analysis. Prepared expert report of findings and attended mediation. The construction involved the construction of six (6) residential housing units at CWRU. The project cost exceeded \$100 million. | | | |
| b. (1) TITLE AND LOCATION (City and State) Wooster Water Pollution Control Plant Wooster, OH | PROFESSIONAL SERVICES 2007 | CONSTRUCTION (If applicable) 2007 | 6 |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Management and settlement strategy advice The project consisted of major renovation and upgrades to the City's water treatment facilities. The project cost exceeded \$15,000,000. | | | |
| c. (1) TITLE AND LOCATION (City and State) 26 th Ward Water Treatment Plant New York, NY | PROFESSIONAL SERVICES 2008 | CONSTRUCTION (If applicable) | 7 |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Project site visit, strategy, and management oversight The project consisted of new construction and the upgrade of water treatment facilities at this 26 th Ward Water Treatment Plant. The project exceeded \$21,000,000. | | | |
| d. (1) TITLE AND LOCATION (City and State) Baruch College New York, NY | PROFESSIONAL SERVICES 2011 | CONSTRUCTION (If applicable) 2002 | 9 |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Project Role: Project lead management oversight, schedule and damages analysis mediation presentation, deposition testimony, analysis of opposing expert reports and rebuttal reports Baruch College is a 16-story vertical campus building in New York City. The approximate project cost exceeded \$250,000,000. | | | |
| e. (1) TITLE AND LOCATION (City and State) | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input type="checkbox"/> Check if project performed with current firm | | | |

E. RESUMES OF KEY PERSONNEL PROPOSED FOR THIS CONTRACT

(Complete one Section E for each key person.)

| | | | |
|---|--|--|----------------------------|
| 16. NAME Dennis R. Jasinski | 17. ROLE IN THIS CONTRACT Project Lead / Expert Witness | 18. YEARS EXPERIENCE | |
| | | a. TOTAL 29 | b. WITH CURRENT FIRM 24 |
| 19. FIRM NAME AND LOCATION (City and State) RV Buric Construction Management Consultants, Inc. Chagrin Falls, OH | | | |
| 20. EDUCATION (DEGREE AND SPECIALIZATION) BS Civil Engineering Technology | | 21. CURRENT PROFESSIONAL REGISTRATION (STATE AND DISCIPLINE) None | |
| 22. OTHER PROFESSIONAL QUALIFICATIONS (Publications, Organizations, Training, Awards, etc.) AIC | | | |

23. RELEVANT PROJECTS (Up to a maximum of 5 samples)

| a. | (1) TITLE AND LOCATION (City and State) | (2) YEAR COMPLETED | | (3) EXAMPLE PROJECT KEY NUMBER (If included in Section F) |
|----|--|-----------------------|------------------------------|---|
| | | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| | Trotwood High School Trotwood, OH | 2009 | 2005 | 1 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Lead consultant – directed and oversaw schedule and damages analysis The construction involved the building of a new high school which had numerous construction defect problems and delay claims. The project cost exceeded \$20,000,000 | | | |
| | Jefferson County Justice Facility Steubenville, OH | | | 2 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Lead consultant – directed and oversaw schedule and damages analysis and expert testimony The project involved the construction of a jail facility, courtrooms, and county offices, amounting to a project cost exceeding \$100,000,000. | | | |
| | Whiskey Island Ore Loader Cleveland, OH | 2006 | 2004-2005 | 4 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Lead consultant – directed and oversaw schedule and damages analysis and expert testimony The project involved the relocation and modification of an ore loader from Lorain to Cleveland, OH. The approximately project cost exceeded \$10,000,000. | | | |
| | Indianapolis Airport Indianapolis, IN | 2009 | 2008-2009 | 8 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Lead consultant – directed and oversaw development of analysis and animated graphics The project involved the construction of large embankments in order to construct new taxiways for the airport. The approximate project cost exceeded \$50 million. | | | |
| | Baruch College New York, NY | 2011 | 2002 | 9 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Developed schedule analysis for key components of overall analysis Baruch College is a 16-story vertical campus building in New York City. The approximate project cost exceeded \$250,000,000. | | | |

E. RESUMES OF KEY PERSONNEL PROPOSED FOR THIS CONTRACT

(Complete one Section E for each key person.)

| | | | |
|---|--|--|---------------------------|
| 16. NAME Andrew Pratt | 17. ROLE IN THIS CONTRACT Senior Project Claims Analyst / Expert Witness | 18. YEARS EXPERIENCE | |
| | | a. TOTAL 29 | b. WITH CURRENT FIRM 4 |
| 19. FIRM NAME AND LOCATION (City and State) RV Buric Construction Management Consultants, Inc. Chagrin Falls, OH | | | |
| 20. EDUCATION (DEGREE AND SPECIALIZATION) BS Quantity Surveying | | 21. CURRENT PROFESSIONAL REGISTRATION (STATE AND DISCIPLINE) None | |
| 22. OTHER PROFESSIONAL QUALIFICATIONS (Publications, Organizations, Training, Awards, etc.) RICS, CIA, CFCC/AACE | | | |

23. RELEVANT PROJECTS (Up to a maximum of 5 samples)

| a. | (1) TITLE AND LOCATION (City and State) | (2) YEAR COMPLETED | | (3) EXAMPLE PROJECT KEY NUMBER (If included in Section F) |
|----|--|-----------------------|------------------------------|---|
| | | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| | Trotwood High School Trotwood, OH | 2009 | 2005 | 1 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Analyzed key issues and co-presented at mediation The construction involved the building of a new high school which had numerous construction defect problems and delay claims. The project cost exceeded \$20,000,000 | | | |
| | 26 th Ward Water Treatment Plant New York, NY | 2009 | | 7 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Schedule cost and impact analysis. Wrote report of findings. The project consisted of new construction and the upgrade of water treatment facilities at this 26 th Ward Water Treatment Plant. The project exceeded \$21,000,000. | | | |
| | Indianapolis Airport Indianapolis, IN | 2009 | 2008-2009 | 8 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Analyze as-built sequence and prepare demonstration oversight and presented analysis at negotiation session. The project involved the construction of large embankments in order to construct new taxiways for the airport. The approximate project cost exceeded \$50 million. | | | |
| | | | | |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input type="checkbox"/> Check if project performed with current firm | | | |
| | | | | |
| | | | | |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input type="checkbox"/> Check if project performed with current firm | | | |

E. RESUMES OF KEY PERSONNEL PROPOSED FOR THIS CONTRACT

(Complete one Section E for each key person.)

| | | | |
|---|--|---|----------------------------|
| 16. NAME Alan Tatro, PE | 17. ROLE IN THIS CONTRACT Senior Project Claims Analyst / Expert Witness | 18. YEARS EXPERIENCE | |
| | | a. TOTAL 32 | b. WITH CURRENT FIRM 17 |
| 19. FIRM NAME AND LOCATION (City and State) RV Buric Construction Management Consultants, Inc. Chagrin Falls, OH | | | |
| 20. EDUCATION (DEGREE AND SPECIALIZATION) BS Civil Engineering | | 21. CURRENT PROFESSIONAL REGISTRATION (STATE AND DISCIPLINE) Ohio Registered Professional Engineer | |
| 22. OTHER PROFESSIONAL QUALIFICATIONS (Publications, Organizations, Training, Awards, etc.) | | | |

23. RELEVANT PROJECTS (Up to a maximum of 5 samples)

| a. | (1) TITLE AND LOCATION (City and State) | (2) YEAR COMPLETED | | (3) EXAMPLE PROJECT KEY NUMBER (If included in Section F) |
|----|--|-----------------------|------------------------------|---|
| | | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| | Case Western Reserve University North Residential Village Cleveland, OH | 2007 | 2005 | 3 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Analyzed structural drawing defects and delay analysis The construction involved the construction of six (6) residential housing units at CWRU. The project cost exceeded \$100 million. | | | |
| | Glen Oak High School Canton, OH | 2006 | 2006 | 5 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Analyzed project schedules and advised client on mediation strategy. Attended mediation. The project value exceeded \$40 million. The project involved the construction of a new high school and library facility and athletic fields. | | | |
| | Wooster Water Pollution Control Plant Wooster, OH | 2007 | 2007 | 6 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Cost, schedule, and productivity analysis. Prepared counter claim damages. The project consisted of major renovation and upgrades to the City's water treatment facilities. The project cost exceeded \$15,000,000. | | | |
| | 26 th Ward Water Treatment Plant New York, NY | 2009 | Incomplete | 7 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Schedule and productivity analyses. Prepared expert report management and oversight The project consisted of new construction and the upgrade of water treatment facilities at this 26 th Ward Water Treatment Plant. The project exceeded \$21,000,000. | | | |
| | Baruch College New York, NY | 2011 | 2002 | 9 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Specific Role: Analyzed structural, exterior sheeting and window specifications, and contracts. Developed delay and production analyses. Prepared report of findings. Baruch College is a 16-story vertical campus building in New York City. The approximate project cost exceeded \$250,000,000. | | | |

E. RESUMES OF KEY PERSONNEL PROPOSED FOR THIS CONTRACT

(Complete one Section E for each key person.)

| | | | |
|--|---|---|---------------------------|
| 16. NAME Joseph Kapitan, AIA | 17. ROLE IN THIS CONTRACT Project Claims Analyst | 18. YEARS EXPERIENCE | |
| | | a. TOTAL 24 | b. WITH CURRENT FIRM 5 |
| 19. FIRM NAME AND LOCATION (City and State) RV Buric Construction Management Consultants, Inc. Chagrin Falls, OH | | | |
| 20. EDUCATION (DEGREE AND SPECIALIZATION) Bachelor of Architecture, MS in Management | | 21. CURRENT PROFESSIONAL REGISTRATION (STATE AND DISCIPLINE) Ohio Registered Architect | |
| 22. OTHER PROFESSIONAL QUALIFICATIONS (Publications, Organizations, Training, Awards, etc.) NCARB Certification, AIA, North Royalton ARB, North Royalton MPTF | | | |

23. RELEVANT PROJECTS (Up to a maximum of 5 samples)

| | (1) TITLE AND LOCATION (City and State) | (2) YEAR COMPLETED | | (3) EXAMPLE PROJECT KEY NUMBER (If included in Section F) |
|----|--|---|------------------------------|---|
| | | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| a. | Trotwood High School Trotwood, OH | 2009 | 2005 | 1 |
| | | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE Analyzed key issues and co-presented at mediation. The construction involved the building of a new high school which had numerous construction defect problems and delay claims. The project cost exceeded \$20,000,000 | | |
| b. | Franklin Township High School Franklin Township, NJ | 2008 | 2005 | |
| | | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE Conducted schedule analysis for a new \$30 million high school in order to refute delay and damages claims made by the structural steel and HVAC prime contractors. Authored expert report. | | |
| c. | Heritage Middle School Painesville, OH | 2009 | 2008 | |
| | | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE Conducted schedule analysis to substantiate general trades prime contractor's defense that it was not responsible for project delays. Presented analysis at mediation. | | |
| d. | Walsh & Kelly Roadway Claims Various locations in Indiana | 2010 | 2009 | |
| | | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE Conducted schedule analysis and compiled damages costs on four separate road reconstruction claims, totaling \$1.5 million. Presented analyses to owner for review and negotiations. | | |
| e. | Massillon Wastewater Treatment Plant Massillon, OH | 2011 | 2005 | |
| | | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE Conducted a limited schedule analysis and analysis of claimed damages presented by Plaintiff (general contractor) and presented defensive ideas to counsel. Attended mediation on behalf of interested third party defendant. Plaintiff's claim was roughly \$5 million. | | |

E. RESUMES OF KEY PERSONNEL PROPOSED FOR THIS CONTRACT

(Complete one Section E for each key person.)

| | | | |
|---|---|--|----------------------------|
| 16. NAME Craig Hutchison | 17. ROLE IN THIS CONTRACT Senior Project Damages Analyst | 18. YEARS EXPERIENCE | |
| | | a. TOTAL 38 | b. WITH CURRENT FIRM 23 |
| 19. FIRM NAME AND LOCATION (City and State) RV Buric Construction Management Consultants, Inc. Chagrin Falls, OH | | | |
| 20. EDUCATION (DEGREE AND SPECIALIZATION) BS Building Design and Construction | | 21. CURRENT PROFESSIONAL REGISTRATION (STATE AND DISCIPLINE) None | |
| 22. OTHER PROFESSIONAL QUALIFICATIONS (Publications, Organizations, Training, Awards, etc.) AACEi, AAA | | | |

23. RELEVANT PROJECTS (Up to a maximum of 5 samples)

| | (1) TITLE AND LOCATION (City and State) | (2) YEAR COMPLETED | | (3) EXAMPLE PROJECT KEY NUMBER (If included in Section F) |
|---|---|-----------------------|------------------------------|---|
| | | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| a. | Case Western Reserve University North Residential Village Cleveland, OH | 2007 | 2005 | 3 |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Developed claims damages and loss of productivity analysis The construction involved the construction of six (6) residential housing units at CWRU. The project cost exceeded \$100 million. | | | | |
| b. | Baruch College New York, NY | 2011 | 2002 | 9 |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Lead consultant for entire damages analysis, oversaw development of analysis and presented at mediation and testified in deposition. Baruch College is a 16-story vertical campus building in New York City. The approximate project cost exceeded \$250,000,000. | | | | |
| c. | | | | |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input type="checkbox"/> Check if project performed with current firm | | | | |
| d. | | | | |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input type="checkbox"/> Check if project performed with current firm | | | | |
| e. | | | | |
| (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input type="checkbox"/> Check if project performed with current firm | | | | |

E. RESUMES OF KEY PERSONNEL PROPOSED FOR THIS CONTRACT

(Complete one Section E for each key person.)

| | | | |
|---|---|--|----------------------------|
| 16. NAME Leslie Sherick Simons | 17. ROLE IN THIS CONTRACT Project Claims Analyst | 18. YEARS EXPERIENCE | |
| | | a. TOTAL 33 | b. WITH CURRENT FIRM 13 |
| 19. FIRM NAME AND LOCATION (City and State) RV Buric Construction Management Consultants, Inc. Chagrin Falls, OH | | | |
| 20. EDUCATION (DEGREE AND SPECIALIZATION) AAS Civil Engineering, Associate Degree in Accounting | | 21. CURRENT PROFESSIONAL REGISTRATION (STATE AND DISCIPLINE) None | |
| 22. OTHER PROFESSIONAL QUALIFICATIONS (Publications, Organizations, Training, Awards, etc.) NAWIC | | | |

23. RELEVANT PROJECTS (Up to a maximum of 5 samples)

| a. | (1) TITLE AND LOCATION (City and State) | (2) YEAR COMPLETED | | (3) EXAMPLE PROJECT KEY NUMBER (If included in Section F) |
|----|---|-----------------------|------------------------------|---|
| | | PROFESSIONAL SERVICES | CONSTRUCTION (If applicable) | |
| | Trotwood High School Trotwood, OH | 2009 | 2005 | 1 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Supported lead consultant and developed key work products The construction involved the building of a new high school which had numerous construction defect problems and delay claims. The project cost exceeded \$20,000,000 | | | |
| | Jefferson County Justice Facility Steubenville, OH | | | 2 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Supported lead consultant and developed key work products The project involved the construction of a jail facility, courtrooms, and county offices, amounting to a project cost exceeding \$100,000,000. | | | |
| | Case Western Reserve University North Residential Village Cleveland, OH | 2007 | 2005 | 3 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Supported lead consultant and developed key work products The construction involved the construction of six (6) residential housing units at CWRU. The project cost exceeded \$100 million. | | | |
| | Baruch College New York, NY | 2011 | 2002 | 9 |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Supported lead consultant and developed key work products Baruch College is a 16-story vertical campus building in New York City. The approximate project cost exceeded \$250,000,000. | | | |
| | Indianapolis Airport Indianapolis, IN | 2009 | 2008-2009 | |
| | (4) BRIEF DESCRIPTION (Brief scope, size, cost, etc.) AND SPECIFIC ROLE <input checked="" type="checkbox"/> Check if project performed with current firm Supported lead consultant and developed key work products The project involved the construction of large embankments in order to construct new taxiways for the airport. The approximate project cost exceeded \$50 million. | | | |

F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT

24. EXAMPLE PROJECT KEY NUMBER (1 – 10)

(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)

| | | |
|---|-----------------------|------------------------------|
| 25. TITLE AND LOCATION <i>(City and State)</i> Trotwood High School Trotwood, OH | 26. YEAR COMPLETED | |
| | PROFESSIONAL SERVICES | CONSTRUCTION (if applicable) |

27. PROJECT OWNER'S INFORMATION

| | | |
|---|---|---|
| a. PROJECT OWNER Trotwood Board of Education | b. POINT OF CONTACT NAME Lowell C. Draffen | c. POINT OF CONTACT TELEPHONE NUMBER (937) 854-3050 X212 |
|---|---|---|

28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT *(Include scope, size, and cost)*

The relevance of the project is to demonstrate Buric's ability to develop and analyze delay claims from a defensive position. Trotwood Board of Education was faced with contractor delay claims and extensive costs of performing corrective repairs resulting from poor workmanship. Buric analyzed the opposing delay claims, developed an analysis of the claimed issues, and developed a rebuttal report. Buric presented its analysis at mediation. The matter was resolved at mediation on behalf of the school board. The construction involved the building of a new high school which had numerous construction defect problems and delay claims. The project cost exceeded \$20,000,000.

29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT

| | | | |
|----|---|--|---|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Schedule and Damages Analysis |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

| | | |
|---|---|---|
| F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT <i>(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)</i> | | 24. EXAMPLE PROJECT KEY NUMBER (1 – 10) |
| 25. TITLE AND LOCATION <i>(City and State)</i> Jefferson County Justice Facility Steubenville, OH | | 26. YEAR COMPLETED PROFESSIONAL SERVICES CONSTRUCTION (if applicable) |
| 27. PROJECT OWNER'S INFORMATION | | |
| a. PROJECT OWNER Jefferson County | b. POINT OF CONTACT NAME Jack Rosati | c. POINT OF CONTACT TELEPHONE NUMBER (614) 227-2321 |
| 28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT <i>(Include scope, size, and cost)</i> | | |

The relevance of this project demonstrates Buric's ability to develop and analyze complicated delay claims in a defensive role. Buric developed a complete schedule analysis for the owner (Jefferson County) and expert report in defense of contractor claims. Buric analyzed owner damages and allocated responsibility for the damages to the responsible parties (contractors and architect). Buric provided expert testimony in federal court. Award of damages was made to the County via a jury verdict at trial. The project involved the construction of a jail facility, courtrooms, and county offices, amounting to a project cost exceeding \$100,000,000.

| 29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT | | | |
|---|---|--|--|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Schedule and Damages Analyses / Expert Witness |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT

(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)

24. EXAMPLE PROJECT KEY NUMBER (1 – 10)

| | | |
|---|-----------------------|------------------------------|
| 25. TITLE AND LOCATION <i>(City and State)</i> Case Western Reserve University North Residential Village Cleveland, OH | 26. YEAR COMPLETED | |
| | PROFESSIONAL SERVICES | CONSTRUCTION (if applicable) |

27. PROJECT OWNER'S INFORMATION

| | | |
|---|---------------------------------------|--|
| a. PROJECT OWNER Case Western Reserve University | b. POINT OF CONTACT NAME Tony Moag | c. POINT OF CONTACT TELEPHONE NUMBER (440) 449-9200 |
|---|---------------------------------------|--|

28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT *(Include scope, size, and cost)*

The relevance of the project is to demonstrate Buric's ability to analyze the impact of design changes and design deficiencies. Buric was retained by Whiting-Turner to analyze drawing changes and prepare impact claims due to inadequate architectural or structural designs. Buric provided cost and schedule analysis services. Buric also attended the mediation. The construction involved the construction of six (6) residential housing units at CWRU. The project cost exceeded \$100 million.

29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT

| | | | |
|----|---|--|--|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Cost and schedule analysis |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

| | |
|---|---|
| F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT <i>(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)</i> | 24. EXAMPLE PROJECT KEY NUMBER (1 – 10) |
|---|---|

| | | |
|---|-------------------------------|---|
| 25. TITLE AND LOCATION <i>(City and State)</i> Whiskey Island Ore Loader Cleveland, OH | 26. YEAR COMPLETED | |
| | PROFESSIONAL SERVICES 2006 | CONSTRUCTION (if applicable) 2004-2005 |

| | | |
|--|---|--|
| 27. PROJECT OWNER'S INFORMATION | | |
| a. PROJECT OWNER Cuyahoga County Port Authority | b. POINT OF CONTACT NAME Skip Jacobson | c. POINT OF CONTACT TELEPHONE NUMBER (216) 241-8004 x18 |

28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT *(Include scope, size, and cost)*

The relevance of its project demonstrates Buric's abilities to develop and analyze delay claims from a defensive position. Buric developed a complete schedule analysis and expert report for the owner (Cuyahoga County Port Authority) in defense of a contractor's claim. An analysis of the claimed contractor costs and the owner costs was developed. Buric testified to its analysis in arbitration. Award of damages were made to the county via an arbitration panel award. The project involved the relocation and modification of an ore loader from Lorain to Cleveland, OH. The approximately project cost exceeded \$10,000,000.

| | | |
|---|--|--|
| 29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT | | |
|---|--|--|

| | | | |
|----|---|--|--|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Schedule and Damages Analyses / Expert Witness |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

| | |
|---|---|
| F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT <i>(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)</i> | 24. EXAMPLE PROJECT KEY NUMBER (1 – 10) |
|---|---|

| | | |
|---|-------------------------------|--------------------------------------|
| 25. TITLE AND LOCATION <i>(City and State)</i> Glen Oak High School Canton, OH | 26. YEAR COMPLETED | |
| | PROFESSIONAL SERVICES 2006 | CONSTRUCTION (if applicable) 2006 |

| | | |
|---|--|--|
| 27. PROJECT OWNER'S INFORMATION | | |
| a. PROJECT OWNER Plain Local Schools | b. POINT OF CONTACT NAME John C. Ross | c. POINT OF CONTACT TELEPHONE NUMBER (330) 433-6000 |

28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT *(Include scope, size, and cost)*

The relevance of this project is to demonstrate Buric's ability to analyze contemporaneous project impacts in order to promote effective completion and occupancy multitude schedule facility buildings. Buric was retained through Plain Local Schools' attorney John C. Ross to determine the impact and responsible parties through the analysis of contemporaneous project schedules on a new high school project. Buric attended mediation in the advisory role. The project value exceeded \$40 million. The project involved the construction of a new high school and library facility and athletic fields.

| | | |
|---|--|--|
| 29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT | | |
|---|--|--|

| | | | |
|-----------|---|--|---|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Schedule analysis and mediation support |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

| | |
|---|---|
| F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT <i>(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)</i> | 24. EXAMPLE PROJECT KEY NUMBER (1 – 10) |
|---|---|

| | | |
|---|-------------------------------|--------------------------------------|
| 25. TITLE AND LOCATION <i>(City and State)</i> Wooster Water Pollution Control Plant Wooster, OH | 26. YEAR COMPLETED | |
| | PROFESSIONAL SERVICES 2007 | CONSTRUCTION (if applicable) 2007 |

| | | |
|-------------------------------------|--|--|
| 27. PROJECT OWNER'S INFORMATION | | |
| a. PROJECT OWNER City of Wooster | b. POINT OF CONTACT NAME Ted Bogner | c. POINT OF CONTACT TELEPHONE NUMBER (330) 262-6393 |

28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT *(Include scope, size, and cost)*

The relevance of this project is to demonstrate Buric's ability to both defend an owner against contractor claims and develop counter claims on behalf of the owner. Buric was retained by Bogner Construction on behalf of the City to defend a claim from a contractor on the City's water pollution control plant. Buric developed a schedule analysis and analyzed damages claimed by the contractor. Buric also advised the City on documentation and counterclaim issues and quantification. The project consisted of major renovation and upgrades to the City's water treatment facilities. The project cost exceeded \$15,000,000.

| | | |
|---|--|--|
| 29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT | | |
|---|--|--|

| | | | |
|-----------|---|--|--|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Schedule and damages analysis, defense and counter claim |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

| | | |
|---|---|---|
| F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT <i>(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)</i> | | 24. EXAMPLE PROJECT KEY NUMBER (1 – 10) |
| 25. TITLE AND LOCATION <i>(City and State)</i> 26 th Ward Water Treatment Plant New York, NY | | 26. YEAR COMPLETED PROFESSIONAL SERVICES 2009 CONSTRUCTION (if applicable) Incomplete |
| 27. PROJECT OWNER'S INFORMATION | | |
| a. PROJECT OWNER NYC DEP | b. POINT OF CONTACT NAME Roland Dung | c. POINT OF CONTACT TELEPHONE NUMBER (347) 689-1706 |
| 28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT <i>(Include scope, size, and cost)</i> | | |

This project demonstrates Buric's ability to analyze project delays and damages resulting from severe project extension resulting from extensive project changes. Buric was retained by Schlesinger-Siemens LLC to perform delay and damages analysis for a water treatment plant project located in New York City. Project was extended several years due to many changes. The project consisted of new construction and the upgrade of water treatment facilities at this 26th Ward Water Treatment Plant. The project exceeded \$21,000,000.

| 29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT | | | |
|---|---|--|--|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Contemporaneous schedule analysis and damages calculations |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

| | |
|---|---|
| F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT <i>(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)</i> | 24. EXAMPLE PROJECT KEY NUMBER (1 – 10) |
|---|---|

| | | |
|--|-------------------------------|---|
| 25. TITLE AND LOCATION <i>(City and State)</i> Indianapolis Airport Indianapolis, Indiana | 26. YEAR COMPLETED | |
| | PROFESSIONAL SERVICES 2009 | CONSTRUCTION (if applicable) 2008-2009 |

| | | |
|--|---|---|
| 27. PROJECT OWNER'S INFORMATION | | |
| a. PROJECT OWNER City of Indianapolis | b. POINT OF CONTACT NAME Ted Brunner | c. POINT OF CONTACT TELEPHONE NUMBER (317) 788-6890 x216 |

28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT *(Include scope, size, and cost)*

This project demonstrates Buric's abilities to analyze construction sequence and prepare demonstrative graphics to support a construction delay analysis. All prior attempts by the contractor to demonstrate the impacts to the owner failed. Buric was retained by a contractor to develop demonstrative animated graphics to explain the sequence of work and causal impacts to timely execution of work. An award of damages was made via negotiations with the engineer on behalf of the City. The project involved the construction of large embankments in order to construct new taxiways for the airport. The approximate project cost exceeded \$50 million.

| | | |
|---|--|--|
| 29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT | | |
|---|--|--|

| | | | |
|----|---|--|--|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE As-built schedule analysis and animated demonstrative graphics |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

F. EXAMPLE PROJECTS WHICH BEST ILLUSTRATE PROPOSED TEAM'S QUALIFICATIONS FOR THIS CONTRACT

(Present as many projects as requested by the Contracting Authority, or a maximum of 10 projects, if not specified. Complete one Section F for each project.)

24. EXAMPLE PROJECT KEY NUMBER (1 – 10)

| | | |
|---|-------------------------------|--------------------------------------|
| 25. TITLE AND LOCATION <i>(City and State)</i> Baruch College New York, NY | 26. YEAR COMPLETED | |
| | PROFESSIONAL SERVICES 2011 | CONSTRUCTION (if applicable) 2002 |

27. PROJECT OWNER'S INFORMATION

| | | |
|---------------------------|---|--|
| a. PROJECT OWNER DASNY | b. POINT OF CONTACT NAME John Scarpelino | c. POINT OF CONTACT TELEPHONE NUMBER (860) 277-5295 |
|---------------------------|---|--|

28. BRIEF DESCRIPTION OF PROJECT AND RELEVANCE TO THIS CONTRACT *(Include scope, size, and cost)*

This project demonstrates Buric's ability to analyze large and complex urban construction projects with a multitude of design issues and project changes. Baruch College is a 16-story vertical campus building in New York City. Buric was retained by Travelers Casualty, the surety acting on behalf of the general trade's contractor in its claim for impact due to delays and changes beyond its control. Buric performed a delay analysis, damages analysis, presented the analyses at mediation, and testified as an expert witness at deposition. The approximate project cost exceeded \$250,000,000.

29. FIRMS FROM SECTION C INVOLVED WITH THIS PROJECT

| | | | |
|----|---|--|---|
| a. | (1) FIRM NAME RV Buric Construction Management Consultants, Inc. | (2) FIRM LOCATION <i>(City and State)</i> Chagrin Falls, OH | (3) ROLE Schedule, damages, and contract balance analysis and expert witness |
| b. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| c. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| d. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| e. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |
| f. | (1) FIRM NAME | (2) FIRM LOCATION <i>(City and State)</i> | (3) ROLE |

F. RELEVANT PROJECT EXPERIENCE MATRIX

| | | Major Scope of Work requirements as identified in the project advertisement. | | | | | | | | | |
|--|--|--|--------|--------|--------|--------|--------|--------|--------|--------|--------|
| | | Scope: | Scope: | Scope: | Scope: | Scope: | Scope: | Scope: | Scope: | Scope: | Scope: |
| Example Project Name (Place "X" under Project Scope) | | | | | | | | | | | |
| 1 | | | | | | | | | | | |
| 2 | | | | | | | | | | | |
| 3 | | | | | | | | | | | |
| 4 | | | | | | | | | | | |
| 5 | | | | | | | | | | | |
| 6 | | | | | | | | | | | |
| 7 | | | | | | | | | | | |
| 8 | | | | | | | | | | | |
| 9 | | | | | | | | | | | |
| 10 | | | | | | | | | | | |

H. ADDITIONAL INFORMATION

34a. PROVIDE ANY ADDITIONAL INFORMATION REQUESTED BY THE CONTRACTING AUTHORITY. ATTACH ADDITIONAL SHEETS AS NEEDED.

H. ADDITIONAL INFORMATION

34b. PROVIDE ANY ADDITIONAL INFORMATION REQUESTED BY THE CONTRACTING AUTHORITY. ATTACH ADDITIONAL SHEETS AS NEEDED.

PROPOSER AFFIRMATION AND DISCLOSURE

The Lead Firm or Joint Venture (“Proposer”) acknowledges that by signing this Statement of Qualifications, that it affirms, understands, and will abide by the requirements of Executive Order 2010-09S issued by Ohio Governor Ted Strickland. If awarded a Contract, the Proposer affirms that both the Proposer and its Consultants shall perform no services requested under the Agreement outside of the United States. The Executive Order is available at the following Web site: <http://www.governor.ohio.gov/Default.aspx?tabid=1495>.

The Proposer shall provide the locations where services under the Contract will be performed in the spaces provided below or by attachment. Failure to provide this information as part of its Statement of Qualifications will cause the Proposer to be deemed non-responsive and no further consideration will be given to its Statement of Qualifications. If the Proposer will not be using Consultants, indicate “Not Applicable” in the appropriate spaces.

1. Principal business location of the Proposer:

300 Park Place
Address

Chagrin Falls, OH 44022
City, State, Zip

2. Location where services will be performed by Proposer:

300 Park Place
Address

Chagrin Falls, OH 44022
City, State, Zip

Locations where services will be performed by Consultants:

Address

City, State, Zip

Address

City, State, Zip

Address

City, State, Zip

3. Location where state data will be stored, accessed, tested, maintained, or backed-up, by Proposer:

300 Park Place
Address

Chagrin Falls, OH 44022
City, State, Zip

Locations where state data will be stored, accessed, tested, maintained, or backed-up by Consultants:

Address

City, State, Zip

Address

City, State, Zip

Address

City, State, Zip

H. ADDITIONAL INFORMATION

34c. PROVIDE ANY ADDITIONAL INFORMATION REQUESTED BY THE CONTRACTING AUTHORITY. USE THE NEXT PAGE OR ATTACH ADDITIONAL SHEETS AS NEEDED.

**COMMITMENT TO PARTICIPATE
IN THE
EDGE BUSINESS ASSISTANCE PROGRAM**

Professional Services Firm: Mark only one option.

Use “✓” or “X” to mark option included in contract award amount.

If marking Option B, also show percentage of proposed participation.

Option A

The Lead Firm or Joint Venture (“Proposer”) commits to *meet or exceed* the advertised EDGE Participation Goal of the award amount, calculated as a portion of the Basic Fee plus all accepted Additional Service Fees and Reimbursable Expenses, by using EDGE-certified Business Enterprise(s).

The Proposer agrees that if selected for consideration of the Contract, it shall provide to the Contracting Authority, at the location required within 10 business days after receiving notice from the Contracting Authority, its Technical Proposal, including a *Certified Statement of Intent To Contract and To Perform* form for each EDGE-certified Business Enterprise proposed for use by the Proposer if awarded the Contract for this Project.

Option B (also indicate percentage -- see text)

The Proposer *does not meet* the advertised EDGE Participation Goal percentage, but, if awarded the Contract for this Project, *commits to provide* _____ **percent of the Contract award amount**, calculated as a portion of the Basic Fee plus all accepted Additional Service Fees and Reimbursable Expenses, by using EDGE-certified Business Enterprise(s).

The Proposer acknowledges it understands the requirement for it to provide and agrees to provide to the Contracting Authority, if selected for consideration of the Contract, within 10 business days after notice from the Contracting Authority, a letter requesting a waiver of the EDGE participation goal percentage on the Proposer’s letterhead with a detailed *Demonstration of Good Faith* form describing its efforts undertaken prior to submitting its Statement of Qualifications to meet the advertised EDGE Participation Goal percentage for the Contract for this Project, and full documentation to substantiate its efforts.

The Proposer commits to provide to the Contracting Authority at the location required within 10 business days after receiving notice from the Contracting Authority, its Technical Proposal, including a *Certified Statement of Intent To Contract and To Perform* form for each EDGE-certified Business Enterprise proposed for use by the Proposer if awarded the Contract for this Project.

Option C

The Proposer declares that it is an EDGE-certified Business Enterprise and that if awarded the Contract, the EDGE Participation percentage will be 100% of the award amount.

I. AUTHORIZED REPRESENTATIVE
The foregoing is a statement of facts.

35. SIGNATURE

36. DATE

37. NAME AND TITLE

STATEMENT OF QUALIFICATIONS

1. PROJECT NUMBER (if any)
DAS 11 D888

PART II – GENERAL QUALIFICATIONS

(If a firm has branch offices, complete for each specific branch office seeking work.)

| | | | | | |
|--|-----------------|---|---|---------------------------------|---|
| 2a. FIRM (OR BRANCH OFFICE) NAME R.V. Buric Construction Management Consultants, Inc. | | | | 3. YR ESTABLISHED 1968 | 4. FTID NUMBER [REDACTED] |
| 2b. STREET 300 Park Place | | | | 5. OWNERSHIP | |
| | | | | a. TYPE S - Corporation | |
| 2c. CITY Chagrin Falls | 2d. STATE OH | 2e. ZIP CODE 44022 | 2f. COUNTY Geauga | b. EDGE STATUS Non-certified | |
| 6a. POINT OF CONTACT NAME AND TITLE Dennis Jasinski Project Director | | | 6b. PRESIDENT/CEO William R. Zollinger III, PE | | 7. NAME OF FIRM (if Block 2a is a branch office.) |
| 6c. TELEPHONE NUMBER (440) 247-3700 | | 6d. E-MAIL ADDRESS djasinski@buric.com | | | |
| 8a. FORMER FIRM NAME(S) (if any) | | | | 8b. YR ESTABLISHED | 8c. FTID NUMBER |

| 9. EMPLOYEES BY DISCIPLINE | | | | 10. PROFILE OF FIRM'S EXPERIENCE AND ANNUAL AVERAGE REVENUE FOR LAST 5 YEARS | | |
|----------------------------|-------------------------|---------------------|------------------|--|---------------------------------------|-------------------------------------|
| a. Function Code | b. Discipline | c. No. of Employees | | a. Profile Code | b. Experience | c. Revenue Index Number (see below) |
| | | (1) LICENSED | (2) NON-LICENSED | | | |
| 06 | Architect | 2 | | A06 | Airports | 3 |
| 12 | Civil Engineer | 5 | 3 | B01 | Barracks | 10 |
| 18 | Cost Engineer/Estimator | | 1 | C10 | Commercial | 5 |
| 42 | Mechanical Engineer | | 1 | C11 | Community Facilities | 1 |
| 53 | Scheduler | | 1 | E02 | Educational Facilities | 14 |
| | Quantities Surveyor | | 1 | F02 | Field House | 2 |
| | Claims Specialist | | | G01 | Garage | 4 |
| 58 | Technical/Analyst | | 3 | H07 | Highways | 13 |
| | | | | H09 | Hospitals and Medical Facilities | 13 |
| | | | | H10 | Hotel | 6 |
| | | | | H11 | Housing | 3 |
| | | | | I01 | Industrial Facilities | 8 |
| | | | | J01 | Judicial | 5 |
| | | | | L04 | Library | 2 |
| | | | | O01 | Office | 4 |
| | | | | P08 | Prison | 6 |
| | | | | P12 | Power | 4 |
| | | | | W03 | Water Supply Treatment & Distribution | 12 |
| | Other Employees | | | | | |
| Total | | 7 | 10 | | | |

| | | | | | |
|--|---|--|--------------------------------------|---|--|
| 11. ANNUAL AVERAGE PROFESSIONAL SERVICES REVENUES OF FIRM FOR LAST 2 YEARS (Insert revenue index number shown at right) | | PROFESSIONAL SERVICES REVENUE INDEX NUMBER | | | |
| a. Work for this Contracting Authority | 0 | 1. Less than \$50,000 | 6. \$400,000 to less than \$500,000 | 11. \$900,000 to less than \$1,000,000 | |
| b. Other State Work (see instructions) | 0 | 2. \$50,000 to less than \$100,000 | 7. \$500,000 to less than \$600,000 | 12. \$1,000,000 to less than \$2,000,000 | |
| c. Total State Work | 0 | 3. \$100,000 to less than \$200,000 | 8. \$600,000 to less than \$700,000 | 13. \$2,000,000 to less than \$5,000,000 | |
| | | 4. \$200,000 to less than \$300,000 | 9. \$700,000 to less than \$800,000 | 14. \$5,000,000 to less than \$10,000,000 | |
| | | 5. \$300,000 to less than \$400,000 | 10. \$800,000 to less than \$900,000 | 15. \$10,000,000 or greater | |

| | |
|---|--------------------|
| 12. AUTHORIZED REPRESENTATIVE The foregoing is a statement of facts. | |
| a. SIGNATURE | b. DATE 4/19/11 |
| c. NAME AND TITLE Dennis Jasinski Project Director | |

Provide a separate Part II form for each firm or branch office participating on the proposed project team.
